



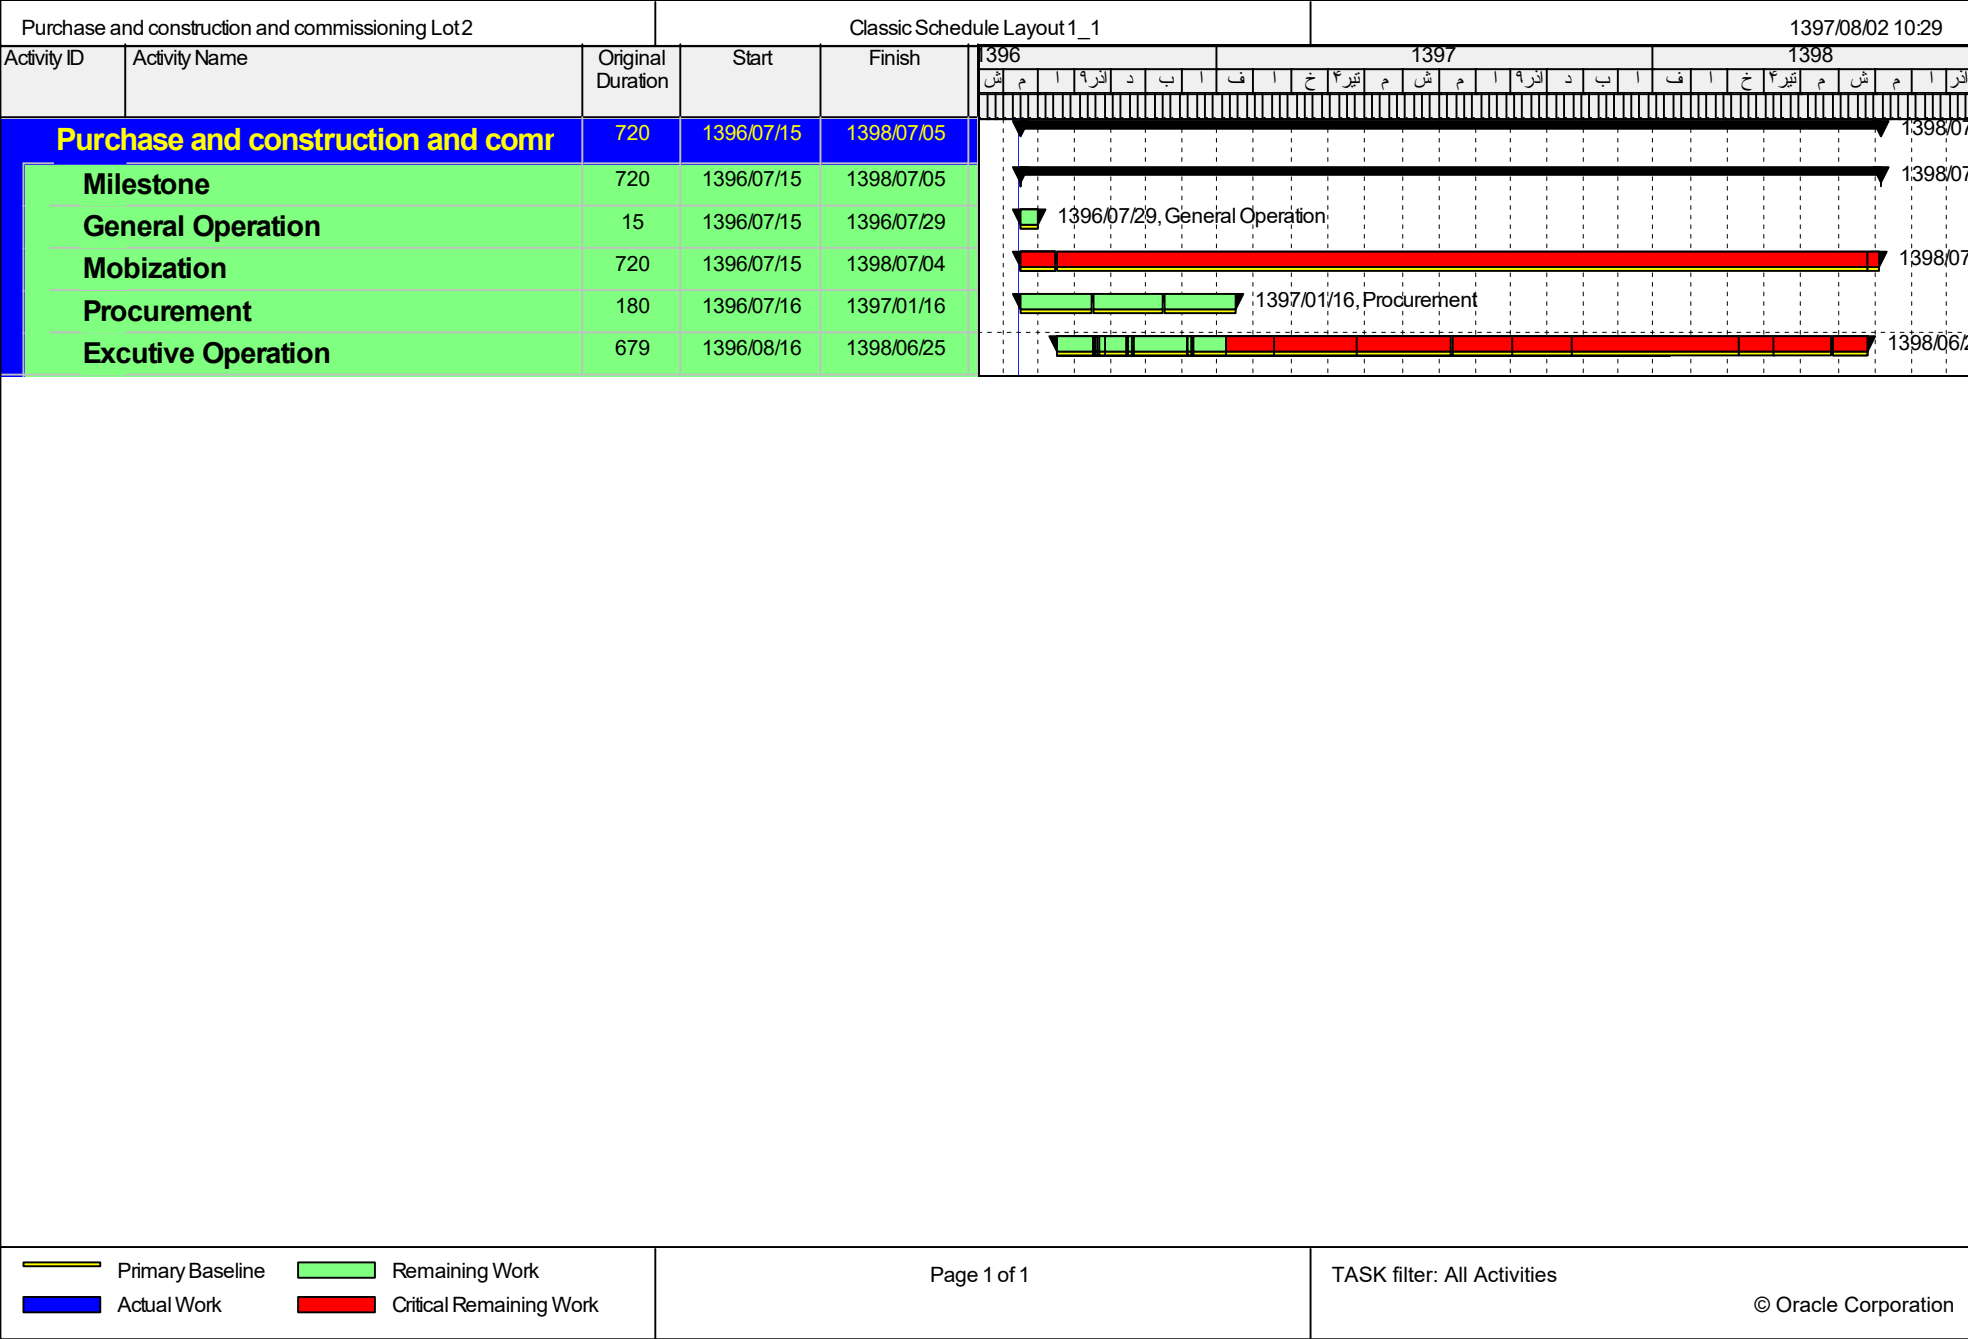

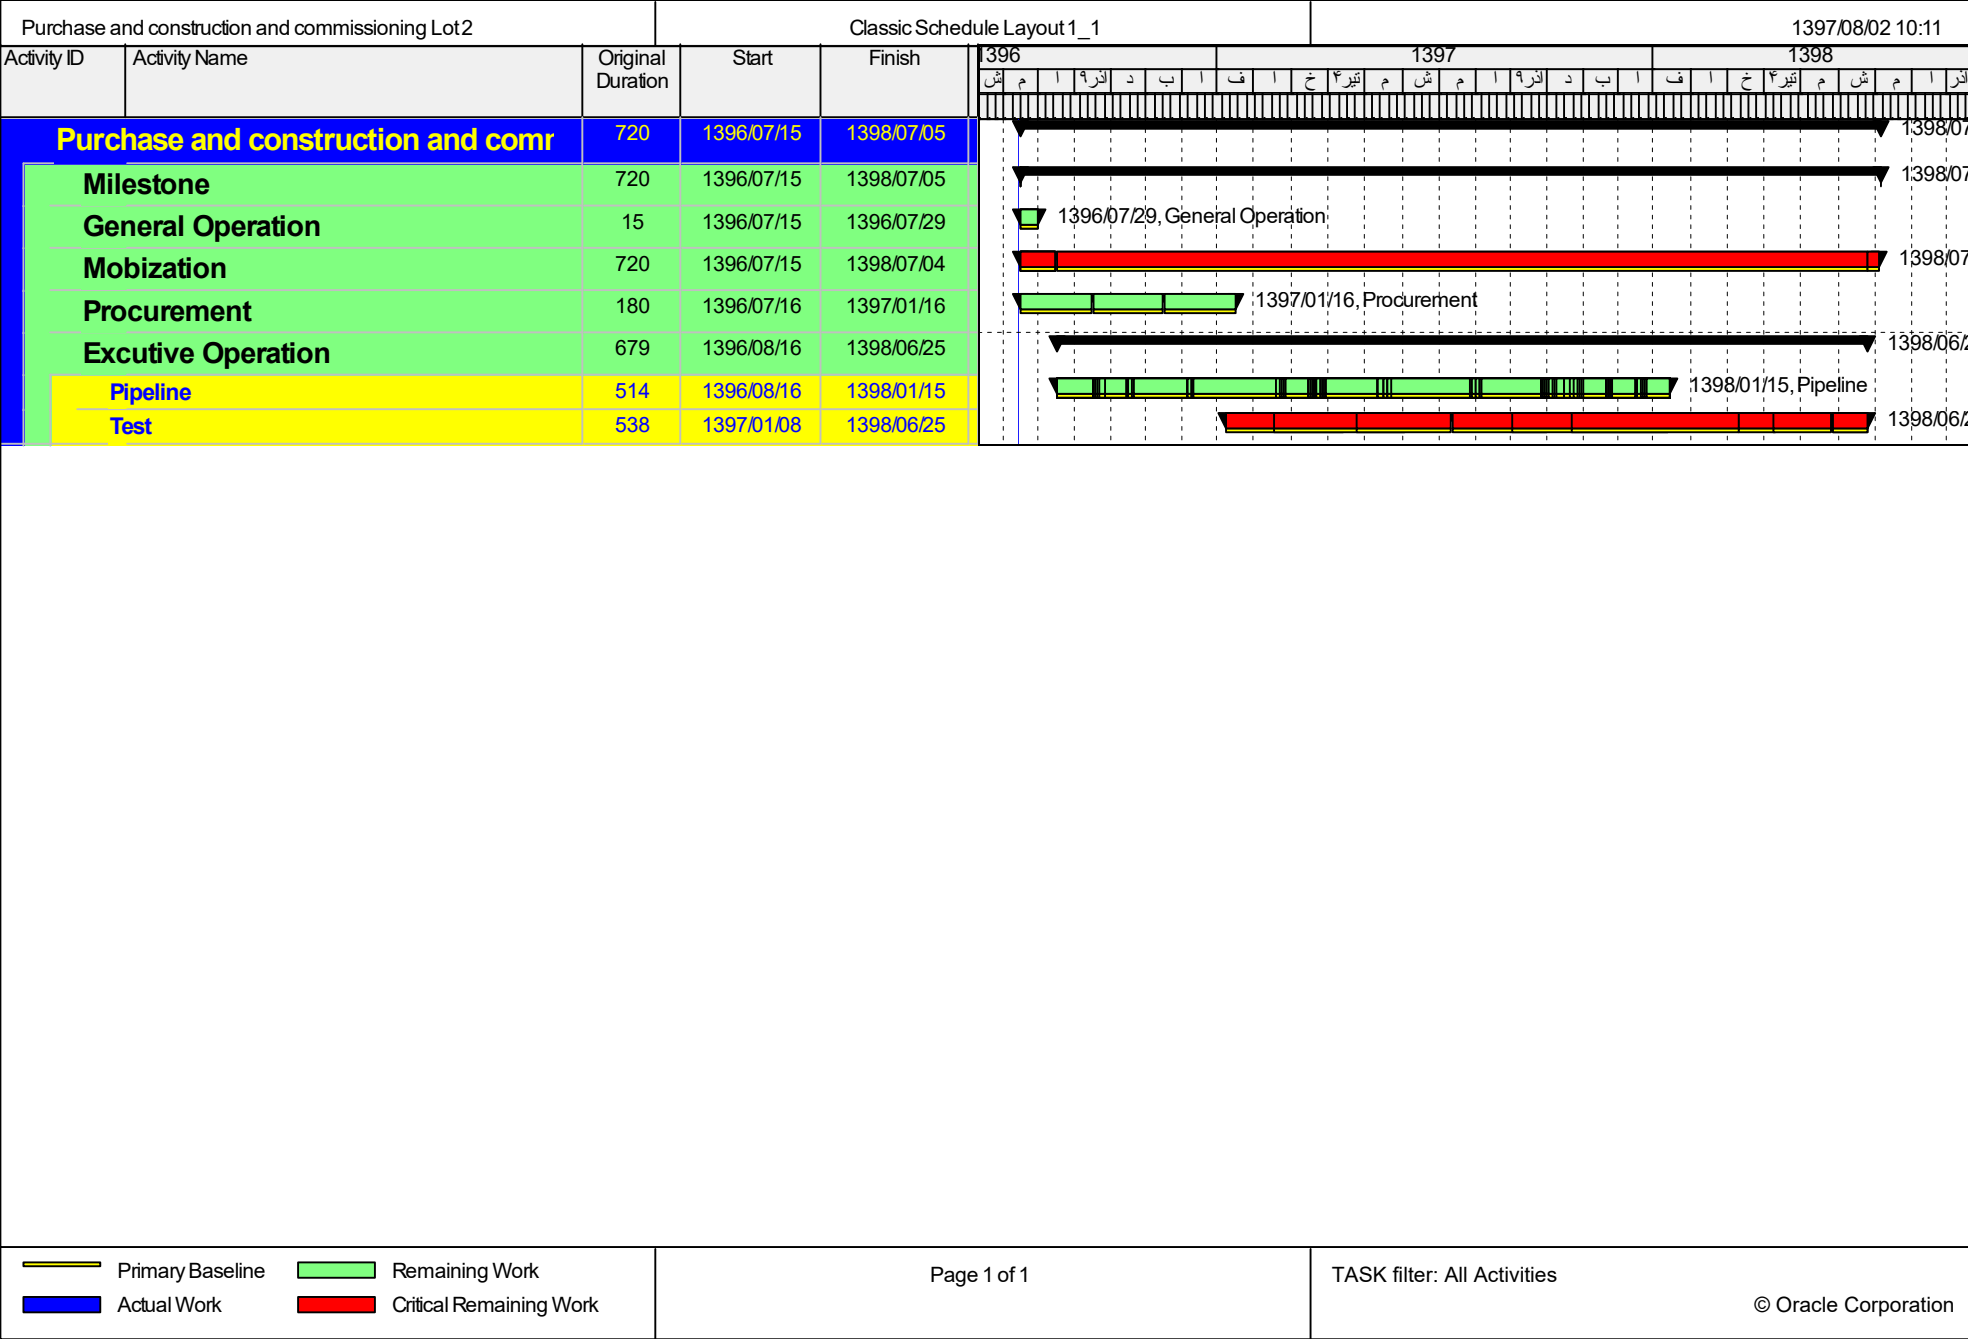

Purchase and construction and commissioning Lot2			Classic Schedule Layout1_1			1397/08/02 10:21																																				
Activity ID	Activity Name	Original Duration	Start	Finish	1396														1397														1398									
					ش م ا ب د ن ر ه ق ف خ ت ث ج ذ ز ح ط ي ل ك غ ص و														ش م ا ب د ن ر ه ق ف خ ت ث ج ذ ز ح ط ي ل ك غ ص و														ش م ا ب د ن ر ه ق ف خ ت ث ج ذ ز ح ط ي ل ك غ ص و									
Purchase and construction and comr			720	1396/07/15	1398/07/05																																					
Milestone			720	1396/07/15	1398/07/05																																					
General Operation			15	1396/07/15	1396/07/29																																					
Mobization			720	1396/07/15	1398/07/04																																					
Procurement			180	1396/07/16	1397/01/16																																					
Excutive Operation			679	1396/08/16	1398/06/25																																					
Pipeline			514	1396/08/16	1398/01/15																																					
Part 1			222	1396/08/16	1397/03/26																																					
Part 8			191	1396/09/16	1397/03/25																																					
Part 2			132	1396/10/14	1397/02/25																																					
Part 3			89	1397/02/20	1397/05/15																																					
Part 7			224	1397/03/21	1397/10/30																																					
Part 4			292	1397/03/22	1398/01/10																																					
Part 5			82	1397/05/11	1397/07/30																																					
Part 6			169	1397/07/26	1398/01/15																																					
Part 9			79	1397/10/26	1398/01/15																																					
Part 10			109	1397/09/26	1398/01/15																																					
Test			538	1397/01/08	1398/06/25																																					
Part 1			100	1397/01/08	1397/04/14																																					
Part 8			110	1397/02/17	1397/06/02																																					
Part 2			80	1397/04/25	1397/07/11																																					
Part 3			80	1397/07/12	1397/10/01																																					
Part 7			130	1397/09/02	1398/01/12																																					
Part 4			140	1397/10/22	1398/03/10																																					
Part 5			30	1398/03/11	1398/04/09																																					
Part 6			50	1398/04/08	1398/05/26																																					
Part 9			30	1398/05/27	1398/06/25																																					
Part 10			30	1398/05/27	1398/06/25																																					

Primary Baseline

Actual Work


Remaining Work

Critical Remaining Work

Page 1 of 1

TASK filter: All Activities

© Oracle Corporation

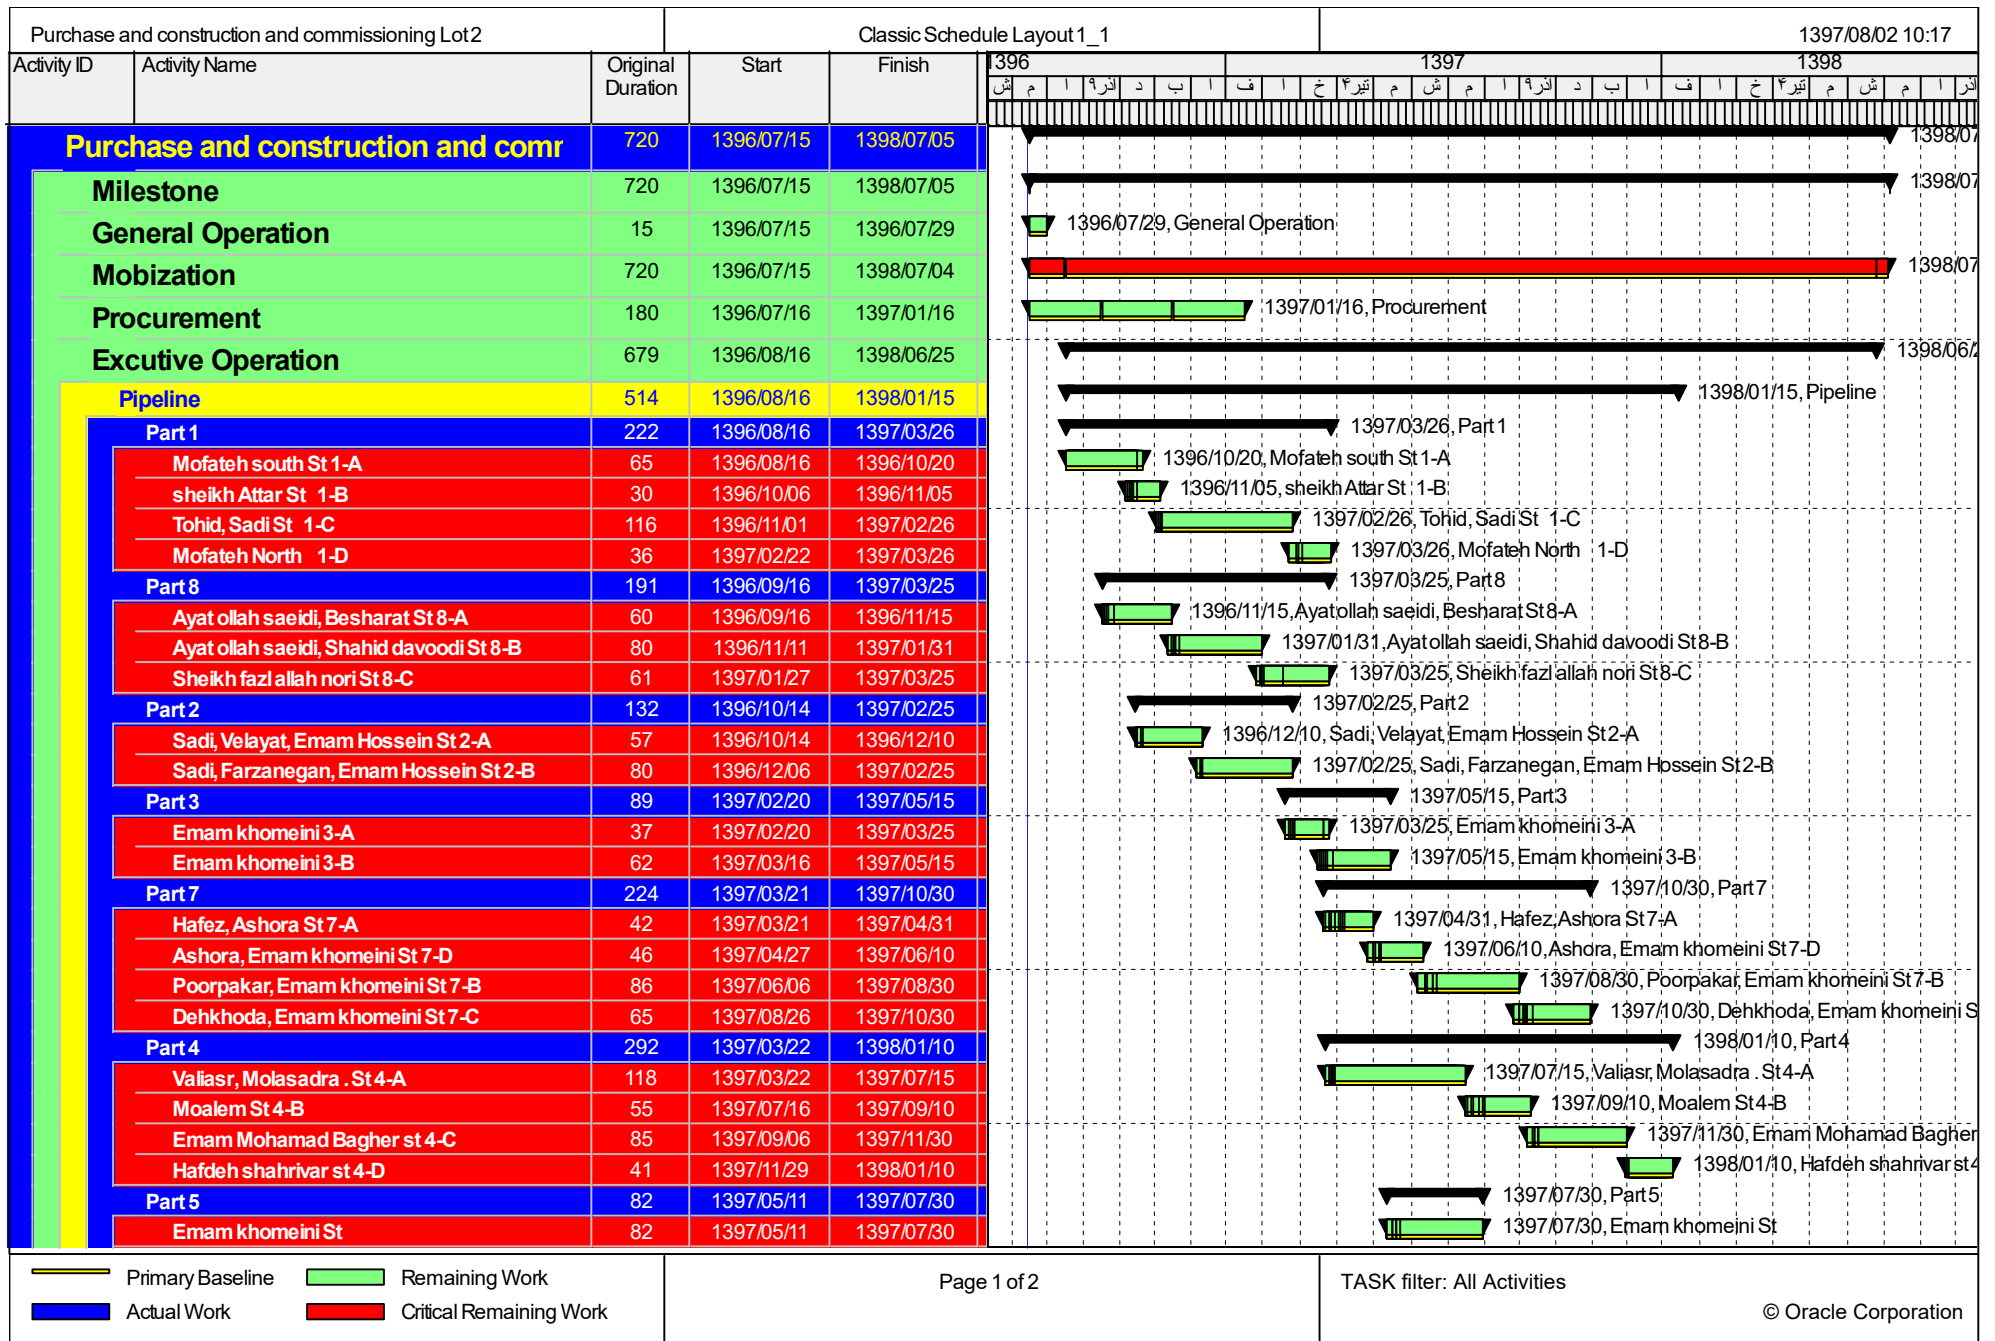

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:17		
Activity ID	Activity Name	Original Duration	Start	Finish	1396	1397	1398	
					ش	م	ش	
	Part 6	169	1397/07/26	1398/01/15			1398/01/15, Part 6	
	South Taleghani St 6-A	100	1397/07/26	1397/11/05			1397/11/05, South Taleghani St 6-A	
	Shahid Abbaspour St 6-B	75	1397/10/30	1398/01/15			1398/01/15, Shahid Abbaspour St 6-B	
	Part 9	79	1397/10/26	1398/01/15			1398/01/15, Part 9	
	Chamran blv	79	1397/10/26	1398/01/15			1398/01/15, Chamran blv	
	Part 10	109	1397/09/26	1398/01/15			1398/01/15, Part 10	
	Emam Khomeini & Azadegan St	20	1397/09/26	1397/10/15			1397/10/15, Emam Khomeini & Azadegan St	
	Farzanegan & Emam Hosein St	36	1397/10/15	1397/11/20			1397/11/20, Farzanegan & Emam Hosein St	
	Daneshgah St	35	1397/11/21	1397/12/25			1397/12/25, Daneshgah St	
	Atash neshani St.	29	1397/12/16	1398/01/15			1398/01/15, Atash neshani St.	
	Test	538	1397/01/08	1398/06/25			1398/06/25, Test	
	Part 1	100	1397/01/08	1397/04/14			1397/04/14, Part 1	
	Part 8	110	1397/02/17	1397/06/02			1397/06/02, Part 8	
	Part 2	80	1397/04/25	1397/07/11			1397/07/11, Part 2	
	Part 3	80	1397/07/12	1397/10/01			1397/10/01, Part 3	
	Part 7	130	1397/09/02	1398/01/12			1398/01/12, Part 7	
	Part 4	140	1397/10/22	1398/03/10			1398/03/10, Part 4	
	Part 5	30	1398/03/11	1398/04/09			1398/04/09, Part 5	
	Part 6	50	1398/04/08	1398/05/26			1398/05/26, Part 6	
	Part 9	30	1398/05/27	1398/06/25			1398/06/25, Part 9	
	Part 10	30	1398/05/27	1398/06/25			1398/06/25, Part 10	

Primary Baseline

Actual Work


Remaining Work

Critical Remaining Work

Page 2 of 2

TASK filter: All Activities

© Oracle Corporation

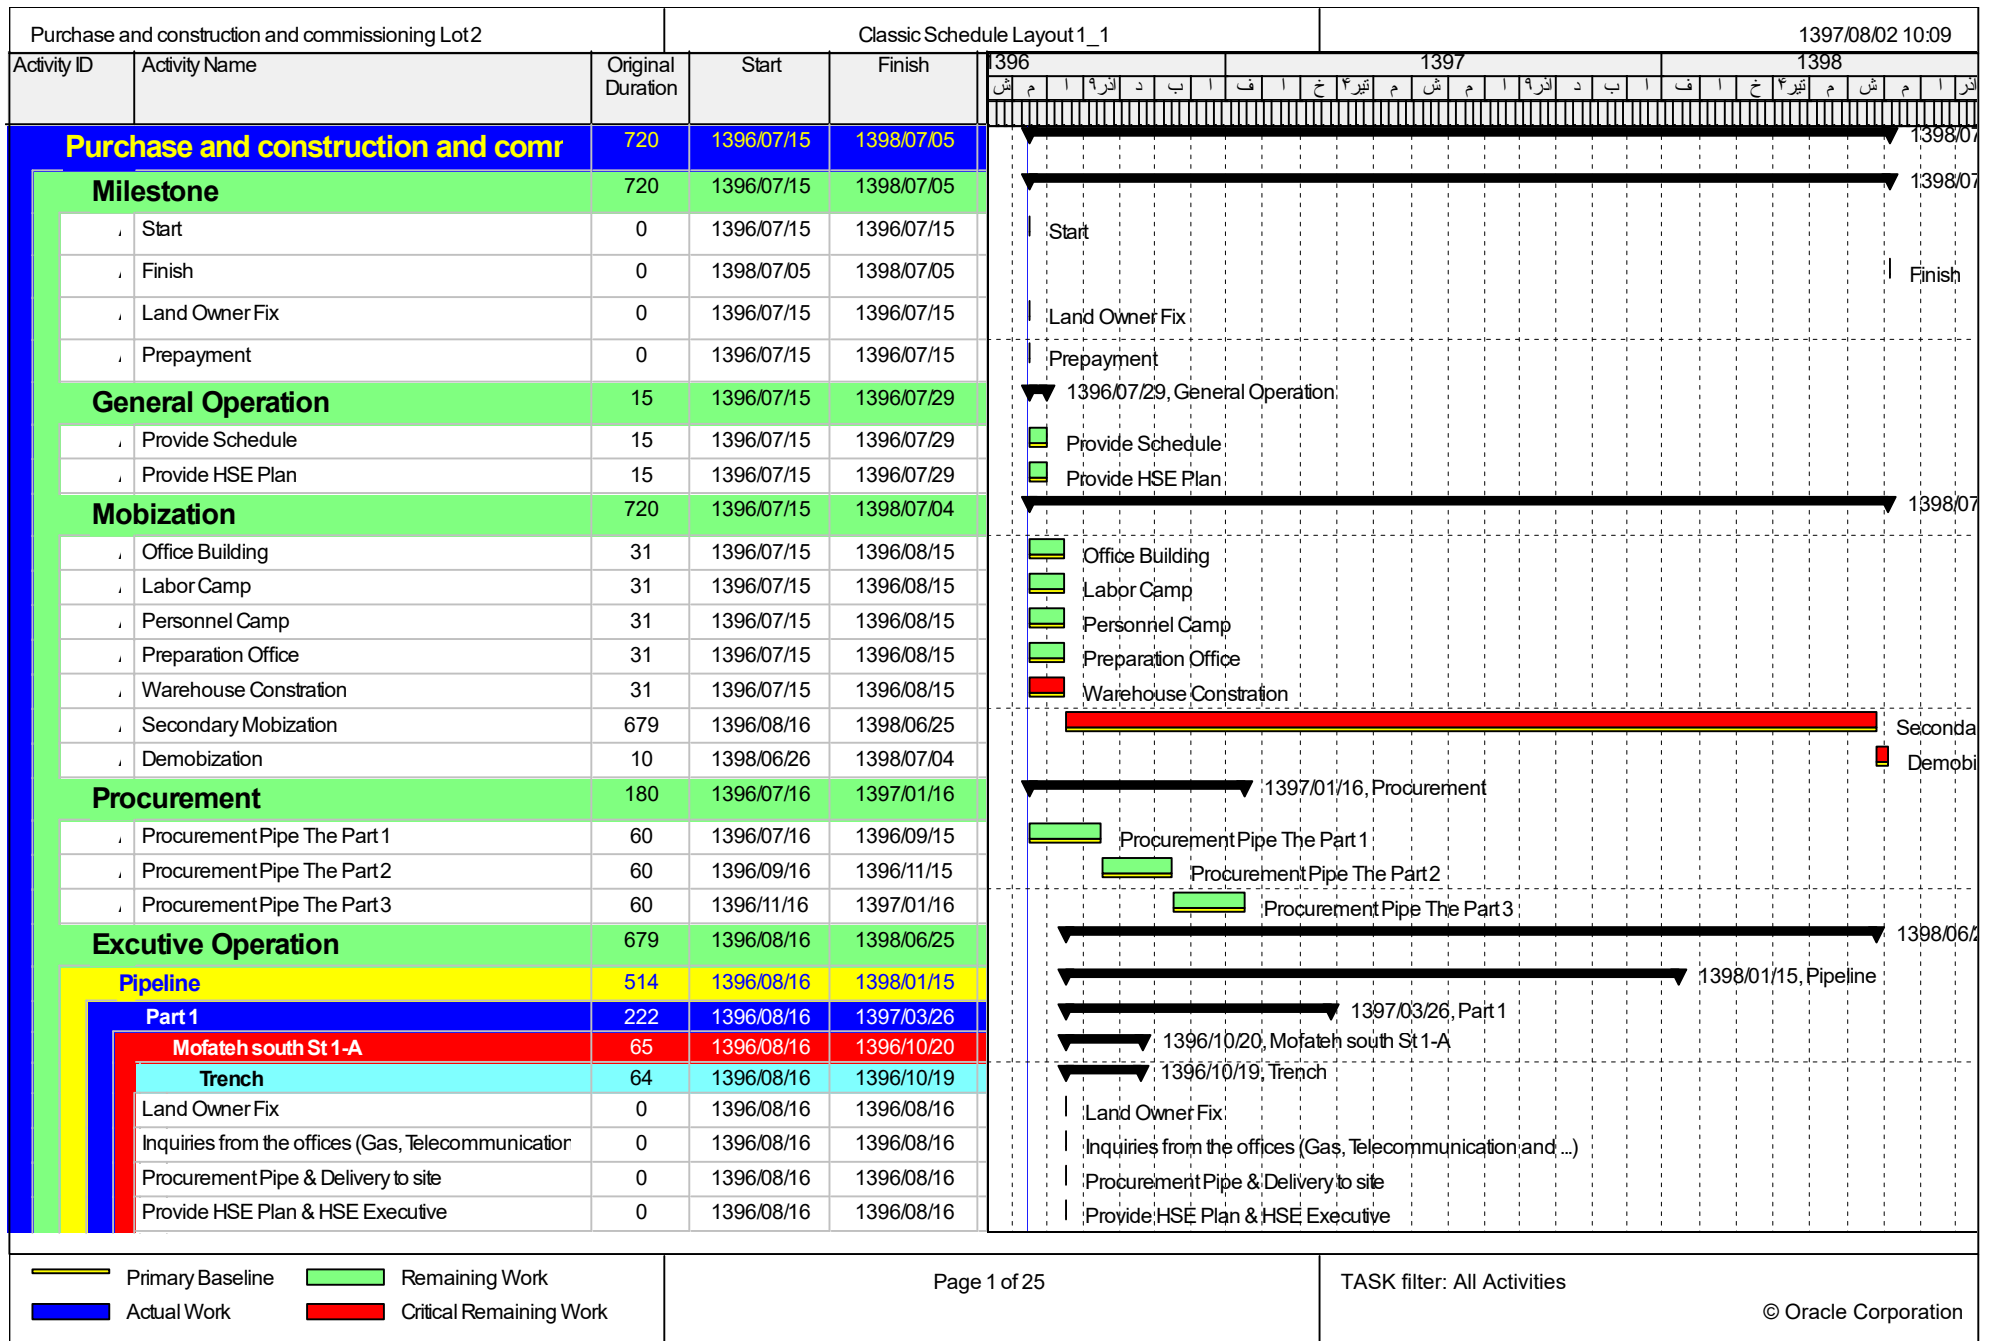

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1					1397/08/02 10:09																								
Activity ID	Activity Name	Original Duration	Start	Finish	1396							1397							1398													
					ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ	ا
	Survey	55	1396/08/16	1396/10/10																												
	Asphalt Cutting	55	1396/08/16	1396/10/10																												
	Trench Excavation	55	1396/08/17	1396/10/11																												
	Loading and Carting Asphalt Scum	55	1396/08/18	1396/10/12																												
	Infrastructure with sand	55	1396/08/19	1396/10/13																												
	Transportation & Row Pipe	55	1396/08/20	1396/10/14																												
	Piping	55	1396/08/21	1396/10/15																												
	Sand on the Pipe	55	1396/08/22	1396/10/16																												
	Backfilling	56	1396/08/23	1396/10/18																												
	Restoration Asphalt	55	1396/08/25	1396/10/19																												
	Completion Operation (Proceedings , Order Work	50	1396/08/26	1396/10/15																												
	Manhole	65	1396/08/16	1396/10/20																												
	Survey	57	1396/08/16	1396/10/12																												
	Construction Foundation at the Workshop (Rebari	57	1396/08/16	1396/10/12																												
	Carting & Erection Foundation	57	1396/08/17	1396/10/13																												
	Brick Wall	57	1396/08/18	1396/10/14																												
	Construction and installation Slab and Gate (Reba	57	1396/08/19	1396/10/15																												
	Backfilling	57	1396/08/20	1396/10/16																												
	Restoration Asphalt	57	1396/08/21	1396/10/17																												
	Completion Operation (Proceedings , Order Work	57	1396/08/24	1396/10/20																												
	House Connection	60	1396/08/16	1396/10/15																												
	Installation House Connection	60	1396/08/16	1396/10/15																												
	sheikh Attar St 1-B	30	1396/10/06	1396/11/05																												
	Trench	30	1396/10/06	1396/11/05																												
	Land Owner Fix	0	1396/10/06	1396/10/06																												
	Inquiries from the offices (Gas, Telecommunication	0	1396/10/06	1396/10/06																												
	Procurement Pipe & Delivery to site	0	1396/10/06	1396/10/06																												
	Provide HSE Plan & HSE Executive	0	1396/10/06	1396/10/06																												
	Survey	22	1396/10/06	1396/10/27																												
	Asphalt Cutting	22	1396/10/06	1396/10/27																												
	Trench Excavation	22	1396/10/07	1396/10/28																												
	Loading and Carting Asphalt Scum	22	1396/10/08	1396/10/29																												
	Infrastructure with sand	22	1396/10/09	1396/10/30																												

— Primary Baseline ■ Remaining Work
■ Actual Work ■ Critical Remaining Work

[illegible]

[illegible]

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:09	
Activity ID	Activity Name	Original Duration	Start	Finish	1396	1397	1398
					ش م ا ن ر د ف ا ب د ا ن ر م ش	ش م ا ن ر د ف ا ب د ا ن ر م ش	ش م ا ن ر د ف ا ب د ا ن ر م ش
	Brick Wall	23	1397/02/29	1397/03/20			
	Construction and installation Slab and Gate (Rebar)	28	1397/02/30	1397/03/26			
	Backfilling	23	1397/03/04	1397/03/26			
	Restoration Asphalt	23	1397/03/04	1397/03/26			
	Completion Operation (Proceedings , Order Work	23	1397/03/04	1397/03/26			
	House Connection	25	1397/03/02	1397/03/26			
	Installation House Connection	25	1397/03/02	1397/03/26			
	Part 8	191	1396/09/16	1397/03/25			
	Ayat ollah saeidi, Besharat St 8-A	60	1396/09/16	1396/11/15			
	Trench	60	1396/09/16	1396/11/15			
	Land Owner Fix	0	1396/09/16	1396/09/16			
	Inquiries from the offices (Gas, Telecommunication	0	1396/09/16	1396/09/16			
	Procurement Pipe & Delivery to site	0	1396/09/16	1396/09/16			
	Provide HSE Plan & HSE Executive	0	1396/09/16	1396/09/16			
	Survey	54	1396/09/16	1396/11/09			
	Asphalt Cutting	54	1396/09/16	1396/11/09			
	Trench Excavation	54	1396/09/17	1396/11/10			
	Loading and Carting Asphalt Scum	54	1396/09/18	1396/11/11			
	Infrastructure with sand	54	1396/09/19	1396/11/12			
	Transportation & Row Pipe	54	1396/09/20	1396/11/13			
	Piping	54	1396/09/21	1396/11/14			
	Sand on the Pipe	53	1396/09/22	1396/11/14			
	Backfilling	54	1396/09/22	1396/11/15			
	Restoration Asphalt	53	1396/09/23	1396/11/15			
	Completion Operation (Proceedings , Order Work	52	1396/09/24	1396/11/15			
	Manhole	60	1396/09/16	1396/11/15			
	Survey	54	1396/09/16	1396/11/09			
	Construction Foundation at the Workshop (Rebar)	55	1396/09/16	1396/11/10			
	Carting & Erection Foundation	55	1396/09/17	1396/11/11			
	Brick Wall	55	1396/09/18	1396/11/12			
	Construction and installation Slab and Gate (Rebar)	55	1396/09/18	1396/11/12			
	Backfilling	55	1396/09/19	1396/11/13			
	Restoration Asphalt	55	1396/09/20	1396/11/14			

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Page 5 of 25

TASK filter: All Activities

© Oracle Corporation

[illegible]

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:09																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
Activity ID	Activity Name	Original Duration	Start	Finish	1396														1397														1398																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																				
					ش	م	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ش	م	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ش	م	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا	ب	ا

Primary Baseline
 Remaining Work
 Actual Work
 Critical Remaining Work

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1					1397/08/02 10:09																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Activity ID	Activity Name	Original Duration	Start	Finish	1396							1397							1398																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																						
					ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ	ا	ش	م	ا	ب	د	خ																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

— Primary Baseline Remaining Work
 Actual Work Critical Remaining Work

[illegible]

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:09		
Activity ID	Activity Name	Original Duration	Start	Finish	1396	1397	1398	
					ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف	ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف	ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف خ م ش م ا ن ر د ا ب ا ف	
	Restoration Asphalt	22	1397/03/04	1397/03/25			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	22	1397/03/04	1397/03/25			Completion Operation (Proceedings , Order Work ,As Built)	
	Manhole	32	1397/02/20	1397/03/20			1397/03/20,Manhole	
	Survey	23	1397/02/20	1397/03/11			Survey	
	Construction Foundation at the Workshop (Rebari	25	1397/02/20	1397/03/13			Construction Foundation at the Workshop (Rebaring , Formwork,Concret	
	Carting & Erection Foundation	23	1397/02/23	1397/03/14			Carting & Erection Foundation	
	Brick Wall	23	1397/02/24	1397/03/15			Brick Wall	
	Construction and installation Slab and Gate (Reba	25	1397/02/25	1397/03/18			Construction and installation Slab and Gate (Rebaring , Formwork,Concert	
	Backfilling	23	1397/02/27	1397/03/18			Backfilling	
	Restoration Asphalt	23	1397/02/28	1397/03/19			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	23	1397/02/29	1397/03/20			Completion Operation (Proceedings , Order Work ,As Built)	
	House Connection	25	1397/02/27	1397/03/20			1397/03/20,House Connection	
	Installation House Connection	25	1397/02/27	1397/03/20			Installation House Connection	
	Emam khomeini 3-B	62	1397/03/16	1397/05/15			1397/05/15, Emam khomeini 3-B	
	Trench	62	1397/03/16	1397/05/15			1397/05/15, Trench	
	Land Owner Fix	0	1397/03/16	1397/03/16			Land Owner Fix	
	Inquiries from the offices (Gas, Telecommunication	0	1397/03/16	1397/03/16			Inquiries from the offices (Gas, Telecommunication and'...	
	Procurement Pipe & Delivery to site	0	1397/03/16	1397/03/16			Procurement Pipe & Delivery to site	
	Provide HSE Plan & HSE Executive	0	1397/03/16	1397/03/16			Provide HSE Plan & HSE Executive	
	Survey	54	1397/03/16	1397/05/07			Survey	
	Asphalt Cutting	54	1397/03/16	1397/05/07			Asphalt Cutting	
	Trench Excavation	55	1397/03/17	1397/05/09			Trench Excavation	
	Loading and Carting Asphalt Scum	54	1397/03/19	1397/05/10			Loading and Carting Asphalt Scum	
	Infrastructure with sand	54	1397/03/20	1397/05/11			Infrastructure with sand	
	Transportation & Row Pipe	54	1397/03/21	1397/05/12			Transportation & Row Pipe	
	Piping	54	1397/03/22	1397/05/13			Piping	
	Sand on the Pipe	53	1397/03/23	1397/05/13			Sand on the Pipe	
	Backfilling	55	1397/03/23	1397/05/15			Backfilling	
	Restoration Asphalt	53	1397/03/25	1397/05/15			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	52	1397/03/26	1397/05/15			Completion Operation (Proceedings , Order Work ,As Built)	
	Manhole	62	1397/03/16	1397/05/15			1397/05/15, Manhole	
	Survey	54	1397/03/16	1397/05/07			Survey	
Construction Foundation at the Workshop (Rebari	56	1397/03/16	1397/05/09			Construction Foundation at the Workshop (Rebaring , Formwork,Co		

Primary Baseline

Actual Work

Remaining Work

Critical Remaining Work

Page 10 of 25

TASK filter: All Activities

© Oracle Corporation

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1					1397/08/02 10:09																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
Activity ID	Activity Name	Original Duration	Start	Finish	1396														1397														1398																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																															
					ش	م	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																														
	Carting & Erection Foundation	55	1397/03/18	1397/05/10																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

— Primary Baseline ■ Remaining Work
■ Actual Work ■ Critical Remaining Work

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:09		
Activity ID	Activity Name	Original Duration	Start	Finish	1396	1397	1398	
					ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف	ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف	ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف خ ن م ش م ا ن ر د ب ا ف	
	Restoration Asphalt	26	1397/04/04	1397/04/29			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	26	1397/04/06	1397/04/31			Completion Operation (Proceedings , Order Work ,As Built)	
	House Connection	25	1397/04/07	1397/04/31			1397/04/31, House Connection	
	Installation House Connection	25	1397/04/07	1397/04/31			Installation House Connection	
	Ashora, Emam khomeini St 7-D	46	1397/04/27	1397/06/10			1397/06/10, Ashora, Emam khomeini St 7-D	
	Trench	46	1397/04/27	1397/06/10			1397/06/10, Trench	
	Land Owner Fix	0	1397/04/27	1397/04/27			Land Owner Fix	
	Inquiries from the offices (Gas, Telecommunication	0	1397/04/27	1397/04/27			Inquiries from the offices (Gas, Telecommunication and ...)	
	Procurement Pipe & Delivery to site	0	1397/04/27	1397/04/27			Procurement Pipe & Delivery to site	
	Provide HSE Plan & HSE Executive	0	1397/04/27	1397/04/27			Provide HSE Plan & HSE Executive	
	Survey	35	1397/04/27	1397/05/30			Survey	
	Asphalt Cutting	35	1397/04/27	1397/05/30			Asphalt Cutting	
	Trench Excavation	36	1397/04/27	1397/05/31			Trench Excavation	
	Loading and Carting Asphalt Scum	35	1397/04/29	1397/06/01			Loading and Carting Asphalt Scum	
	Infrastructure with sand	35	1397/04/30	1397/06/02			Infrastructure with sand	
	Transportation & Row Pipe	35	1397/04/31	1397/06/03			Transportation & Row Pipe	
	Piping	35	1397/05/01	1397/06/04			Piping	
	Sand on the Pipe	35	1397/05/02	1397/06/05			Sand on the Pipe	
	Backfilling	37	1397/05/03	1397/06/08			Backfilling	
	Restoration Asphalt	35	1397/05/06	1397/06/09			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	35	1397/05/07	1397/06/10			Completion Operation (Proceedings , Order Work ,As Built)	
	Manhole	46	1397/04/27	1397/06/10			1397/06/10, Manhole	
	Survey	35	1397/04/27	1397/05/30			Survey	
	Construction Foundation at the Workshop (Rebari	38	1397/04/27	1397/06/02			Construction Foundation at the Workshop (Rebaring, Formwork	
	Carting & Erection Foundation	35	1397/04/31	1397/06/03			Carting & Erection Foundation	
	Brick Wall	35	1397/05/01	1397/06/04			Brick Wall	
	Construction and installation Slab and Gate (Reba	38	1397/05/02	1397/06/08			Construction and installation Slab and Gate (Rebaring , Formwo	
	Backfilling	35	1397/05/05	1397/06/08			Backfilling	
	Restoration Asphalt	35	1397/05/06	1397/06/09			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	35	1397/05/07	1397/06/10			Completion Operation (Proceedings , Order Work ,As Built)	
	House Connection	35	1397/05/07	1397/06/10			1397/06/10, House Connection	
	Installation House Connection	35	1397/05/07	1397/06/10			Installation House Connection	
	Poorpakar, Emam khomeini St 7-B	86	1397/06/06	1397/08/30			1397/08/30, Poorpakar, Emam khomeini St 7-B	

Primary Baseline Remaining Work Actual Work Critical Remaining Work

Page 12 of 25

TASK filter: All Activities

© Oracle Corporation


[illegible]

[illegible]

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1					1397/08/02 10:09																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
Activity ID	Activity Name	Original Duration	Start	Finish	1396					1397					1398																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
					ش	ا	م	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف	ا	ب	د	ف																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										

— Primary Baseline ■ Remaining Work
■ Actual Work ■ Critical Remaining Work

[illegible]

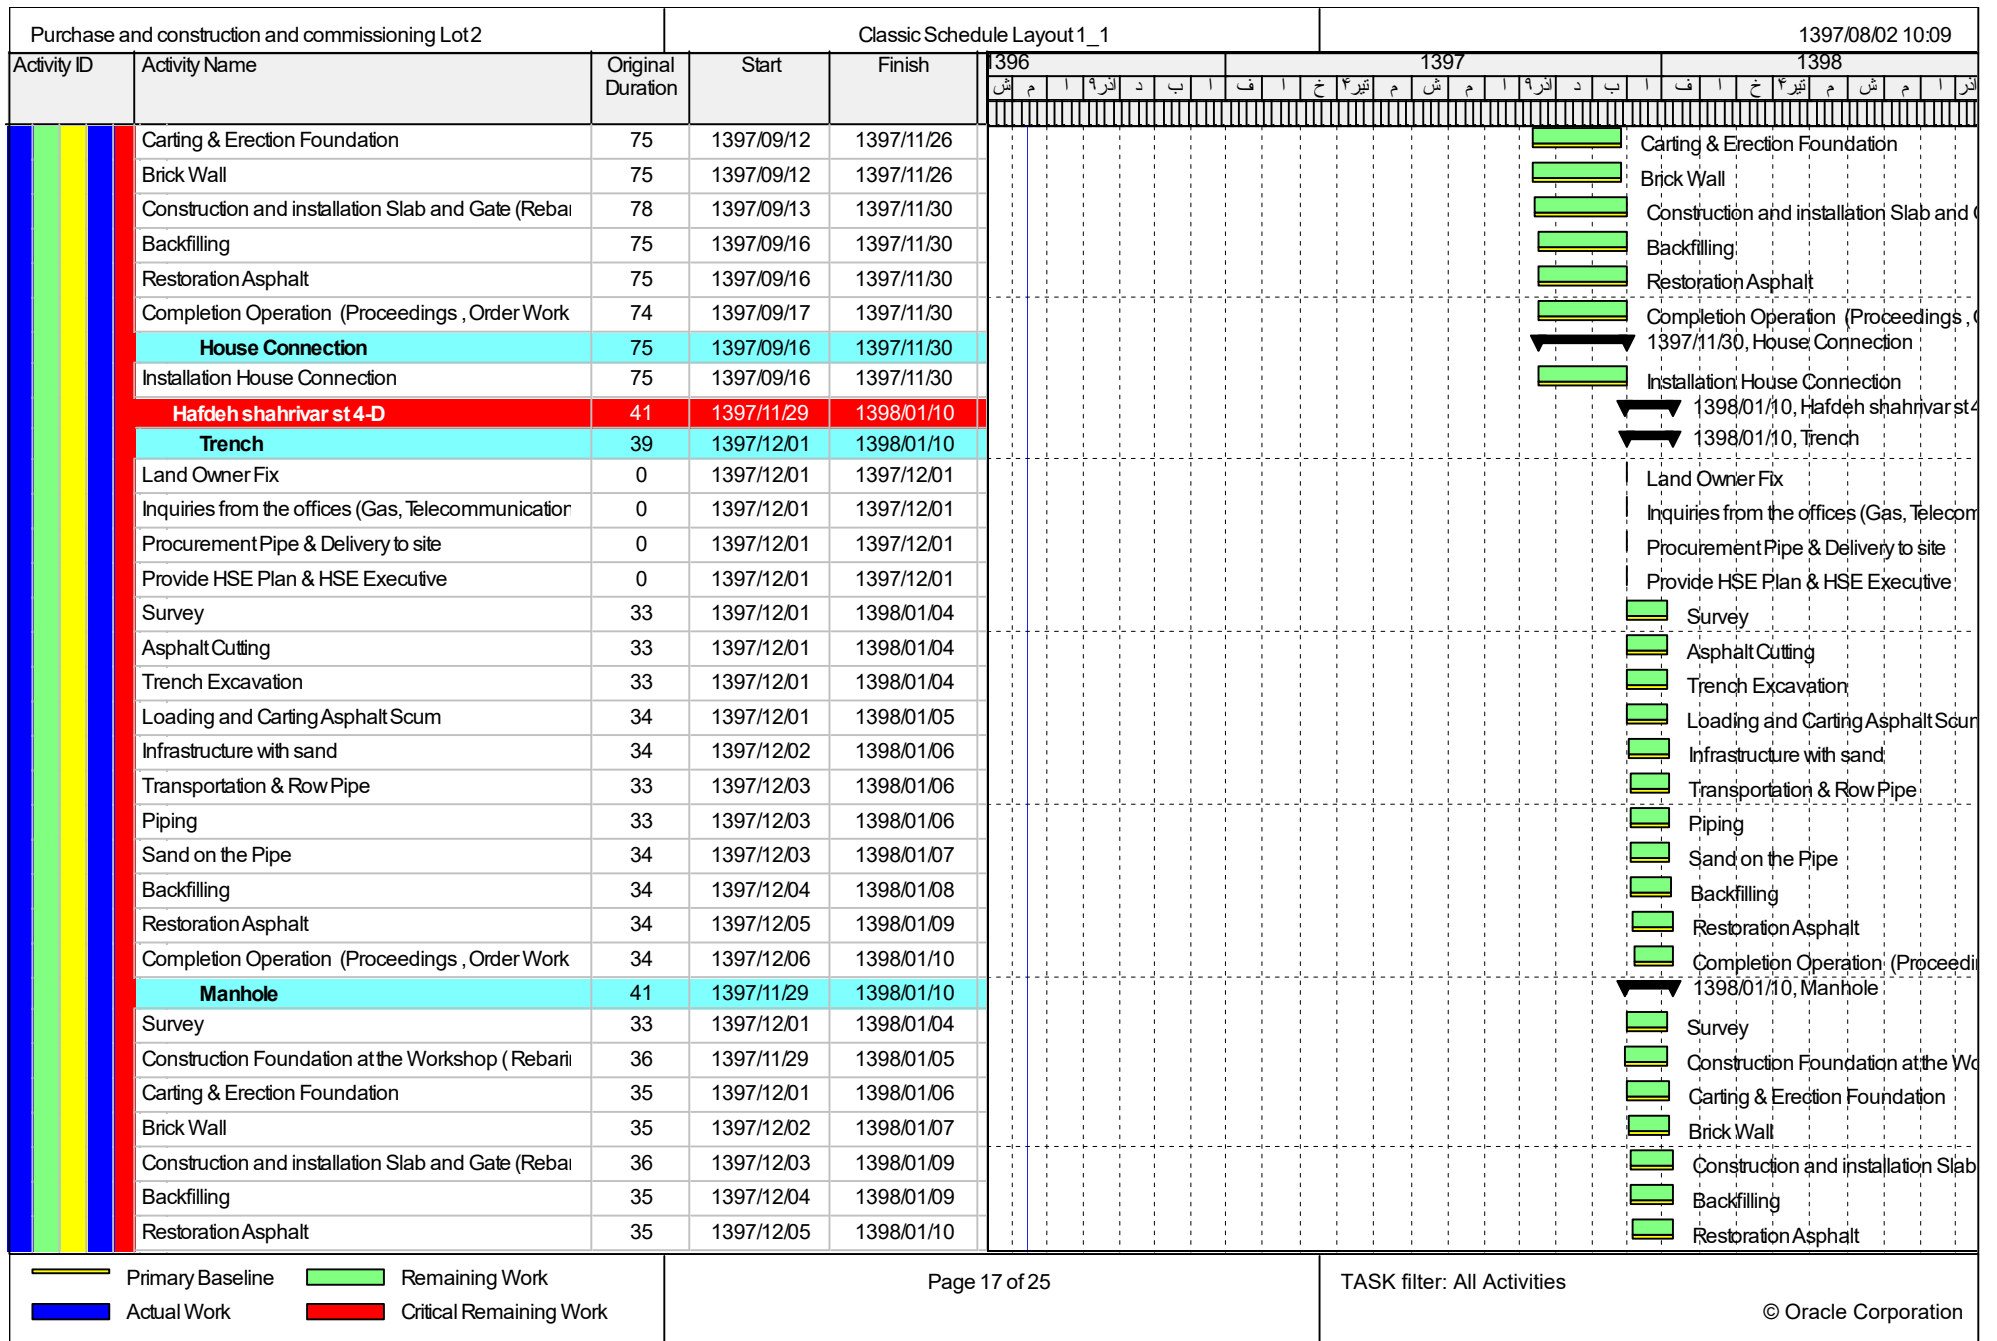

[illegible]

[illegible]

Purchase and construction and commissioning Lot2			Classic Schedule Layout 1_1			1397/08/02 10:09		
Activity ID	Activity Name	Original Duration	Start	Finish	1396	1397	1398	
					ش	م	ش	
	Provide HSE Plan & HSE Executive	0	1397/11/01	1397/11/01			Provide HSE Plan & HSE Executive	
	Survey	60	1397/11/01	1398/01/01			Survey	
	Asphalt Cutting	65	1397/11/01	1398/01/06			Asphalt Cutting	
	Trench Excavation	70	1397/11/01	1398/01/11			Trench Excavation	
	Loading and Carting Asphalt Scum	65	1397/11/06	1398/01/11			Loading and Carting Asphalt Scum	
	Infrastructure with sand	65	1397/11/07	1398/01/12			Infrastructure with sand	
	Transportation & Row Pipe	65	1397/11/08	1398/01/13			Transportation & Row Pipe	
	Piping	65	1397/11/09	1398/01/14			Piping	
	Sand on the Pipe	65	1397/11/04	1398/01/09			Sand on the Pipe	
	Backfilling	75	1397/10/30	1398/01/15			Backfilling	
	Restoration Asphalt	65	1397/11/10	1398/01/15			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	60	1397/11/15	1398/01/15			Completion Operation (Proceedings , Order Work	
	Manhole	74	1397/11/01	1398/01/15			1398/01/15, Manhole	
	Survey	70	1397/11/01	1398/01/11			Survey	
	Construction Foundation at the Workshop (Rebari	74	1397/11/01	1398/01/15			Construction Foundation at the Workshop (Rebari	
	Carting & Erection Foundation	73	1397/11/02	1398/01/15			Carting & Erection Foundation	
	Brick Wall	73	1397/11/02	1398/01/15			Brick Wall	
	Construction and installation Slab and Gate (Rebari	74	1397/11/01	1398/01/15			Construction and installation Slab and Gate (Rebari	
	Backfilling	73	1397/11/02	1398/01/15			Backfilling	
	Restoration Asphalt	73	1397/11/02	1398/01/15			Restoration Asphalt	
	Completion Operation (Proceedings , Order Work	73	1397/11/02	1398/01/15			Completion Operation (Proceedings , Order Work	
	House Connection	68	1397/11/07	1398/01/15			1398/01/15, House Connection	
	Installation House Connection	68	1397/11/07	1398/01/15			Installation House Connection	
	Part9	79	1397/10/26	1398/01/15			1398/01/15, Part9	
	Chamran blv	79	1397/10/26	1398/01/15			1398/01/15, Chamran blv	
	Trench	79	1397/10/26	1398/01/15			1398/01/15, Trench	
	Land Owner Fix	0	1397/10/26	1397/10/26			Land Owner Fix	
	Inquiries from the offices (Gas, Telecommunication	0	1397/10/26	1397/10/26			Inquiries from the offices (Gas, Telecommunication	
	Procurement Pipe & Delivery to site	0	1397/10/26	1397/10/26			Procurement Pipe & Delivery to site	
	Provide HSE Plan & HSE Executive	0	1397/10/26	1397/10/26			Provide HSE Plan & HSE Executive	
	Survey	73	1397/10/26	1398/01/09			Survey	
	Asphalt Cutting	73	1397/10/26	1398/01/09			Asphalt Cutting	
	Trench Excavation	75	1397/10/26	1398/01/11			Trench Excavation	

Primary Baseline

Remaining Work

Actual Work


Critical Remaining Work

Page 20 of 25

TASK filter: All Activities

© Oracle Corporation

[illegible]

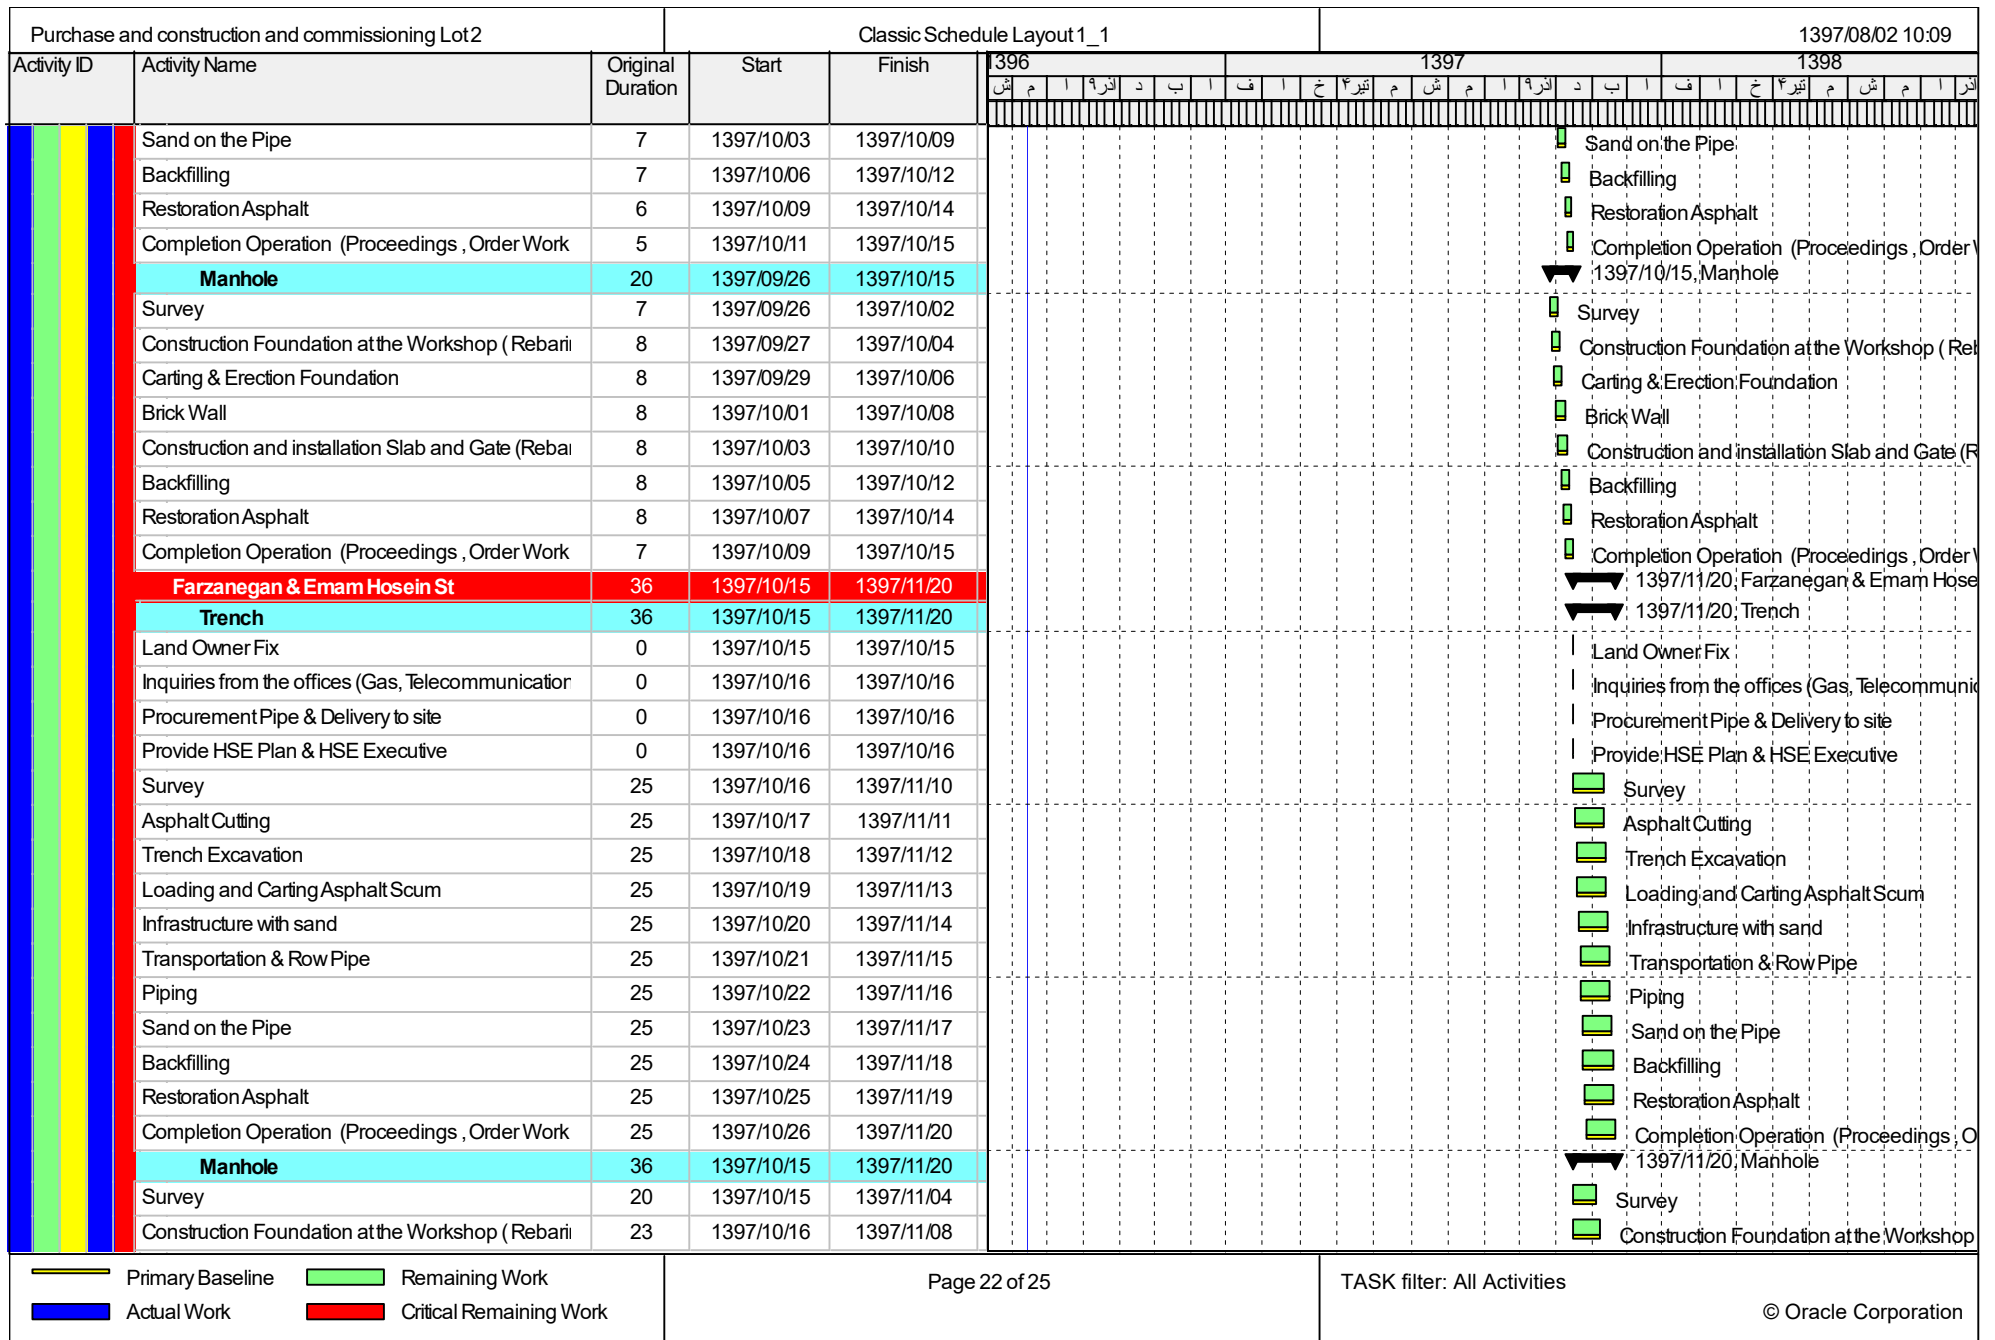

[illegible]

[illegible]

[illegible]
